

Summer Project Update

+

BLUE ● ● ●
VALLEY
2023 BOND



Summer Projects

ABM: New Multipurpose Space, New Intern Office, New Desks

AGE: Painting

BRE: New De-Escalation Room, New Front-Loop Paving

BVA: Painting, Parking Lot Replacement, FACS Renovations (Pre-Construction)

BVH: New Intern Office, Front Office Furniture Remodel, 3d Art Classroom Construction/Renovation, New Weight Room (Pre-Construction), FACS Renovations (Pre-Construction)

BVM: Front Office Furniture Reconfiguration, New Front-Loop Paving

BVN: New Intern Office, Partial Roof Replacement, New Paging System, New Weight Room (Under Construction), Mobile Classroom Demoed, New Band Room Addition (Pre-Construction), FACS Renovations (Pre-Construction)

BVNW: New Intern Office, New HVAC in main and aux gym, New Weight Room (Pre-Construction), FACS Renovations (Pre-Construction)

BVSW: Painting, FACS Renovations (Pre-Construction)

BVW: New Intern Office, New Aux Gym (Under Construction), New Tennis Courts, New Parking Lot, FACS Renovations (Pre-Construction), North Entrance Road Widening (Under Construction), New Art Room Furniture

CAPS: Painting

CHE: Mobile Demo and Classroom Addition (Pre-Construction), New Paging System, SPED Flooring

CPE: Painting, SPED Flooring

HES: New Intern Office, New Paging System

HMS: Building shoring to eliminate settlement cracks, Painting, New Multipurpose Addition (Pre-Construction)

HLC: ECC Classroom Expansion/Renovation (Under Construction), 2nd Floor Office Furniture Replacement

HRT: Painting

IVE: Painting

LKE: Painting

LKM: Furniture Replacement Project

LES: New Intern Office, New Flooring, New Parking Lot (Pre-Construction), Classroom Addition (Pre-Construction), Outdoor Learning PTO Project (In Construction)

LMS: Building-wide Recabling Project Painting

LVE: Painting

MOR: Mobile Classroom Demoed, New Casework and Cubbies in Gifted Classroom

MTE: Painting

OHE: New Intern Office, New Flooring

OTE: Painting, SPED Renovations

OTM: New Intern Office

OMS: Building-wide Recabling Project, New Conference Room

PRM: Painting, New Multipurpose Addition (Pre-Construction)

PSE: New paging system

PSM: Furniture Replacement Project

SPE: Painting, Walking Trail Repairs

SRE: Painting, Walking Trail Repairs

STAN: Painting, Parking Lot Replacement

STIL: Expanded Playground, Painting

TCE: Painting, Mobile Demoed

VPE: New Flooring, SPED Renovations, Front-Loop Pavement Modifications

WSE: Painting, New Intern Office



BLUE ● ● ● VALLEY 2023 BOND

FACILITIES

Additions and New Facilities

- New Middle School
- High School Auxiliary Gyms
- Middle School Multipurpose Additions

Targeted Improvements

- Career & Technical Education
- Early Childhood Expansion
- Special Education Modifications
- Eliminating Elementary School Mobiles

Asset Preservation

- Pavement & Exterior Envelope
- Flooring
- Mechanical

SAFETY

Updated Safety Systems

- Fire Alarm
- Security
- Infrastructure

Upgraded Emergency Communication Systems

TECHNOLOGY

Updated Technology

- Student & Classroom
- Hardware/Software

Upgraded Technology Solutions

- Infrastructure
- Critical Systems/Security



Aubry Bend Multipurpose Addition

BOND 2023



- **Complete July 2024**
- **1st Middle School Multi-Purpose Space**
- **1 of 3 in Bond 2023**



Aubry Bend Multipurpose Addition

BOND 2023



- **ICC 500 Storm Shelter**
- **New rubberized flooring to support non-athletic activities as well as athletics**



Under Construction

BOND 2023



1 BVW Auxiliary Gym



2 BVN Weight Room



3 Hilltop Early Childhood Expansion



BVW Auxiliary Gymnasium

BOND 2023



- **Construction Started May 2024**
- **Anticipated Completion April 2025**



BVW Auxiliary Gymnasium

BOND 2023



- **Construction Started May 2024**
- **Anticipated Completion April 2025**



BVN Weight Room

BOND 2023



- **Construction Started May 2024**
- **Anticipated Completion March 2025**



BVN Weight Room Addition

BOND 2023



- **Construction Started May 2024**
- **Anticipated Completion March 2025**



Hilltop Early Childhood Expansion

BOND 2023




- **Construction Started June 2024**
- **Anticipated Completion December 2024**



Hilltop Early Childhood Expansion


BOND 2023

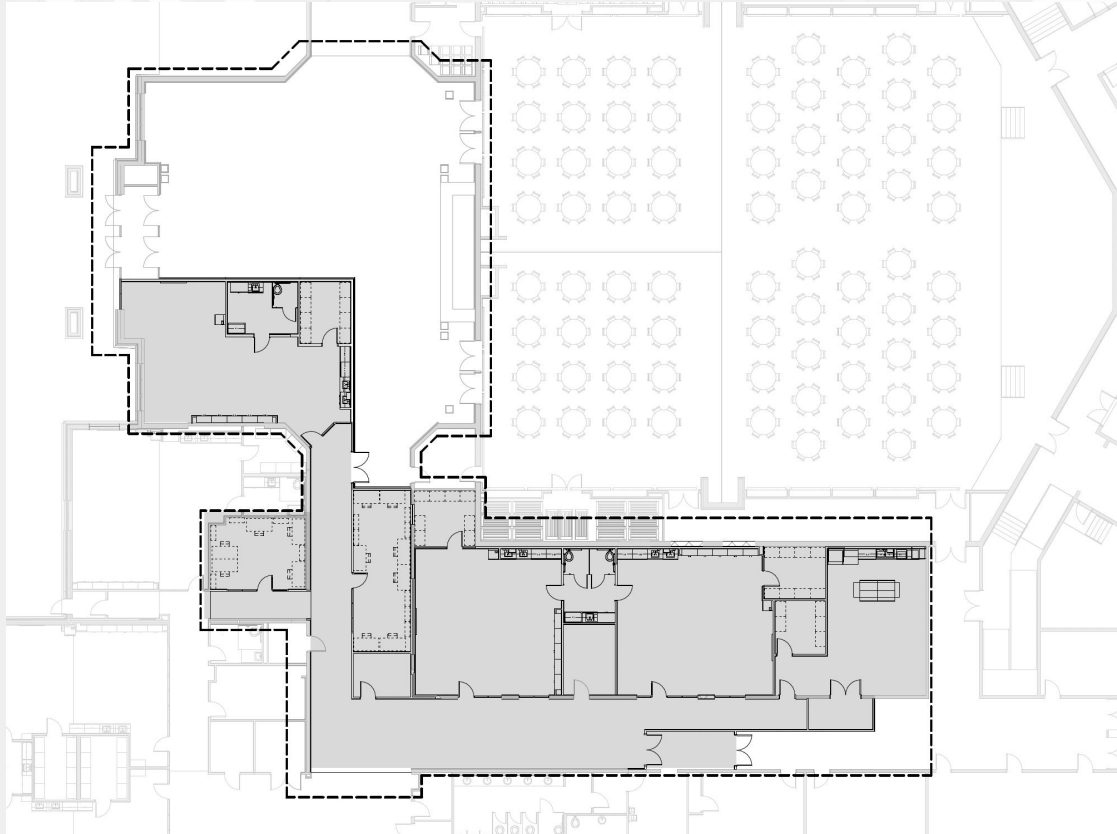

- **Construction Started June 2024**
- **Anticipated Completion December 2024**



BOND 2023

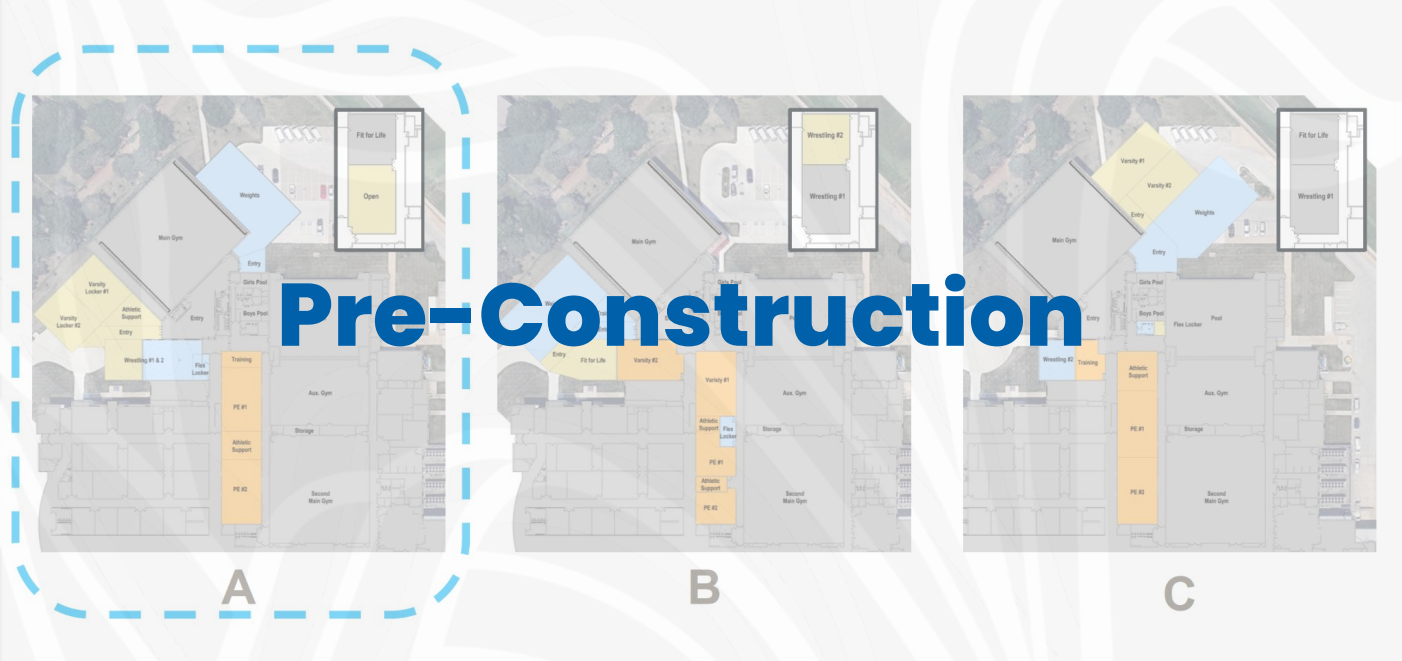

Blue Valley Northwest Weight Room Addition

BOND 2023



- **Anticipated Start
October 2024**
- **Anticipated
Completion
August 2025**



Harmony MS Multipurpose Addition

BOND 2023




- **Anticipated Start
October 2024**
- **Anticipated
Completion
August 2025**



Leawood Elementary Classroom Addition

BOND 2023

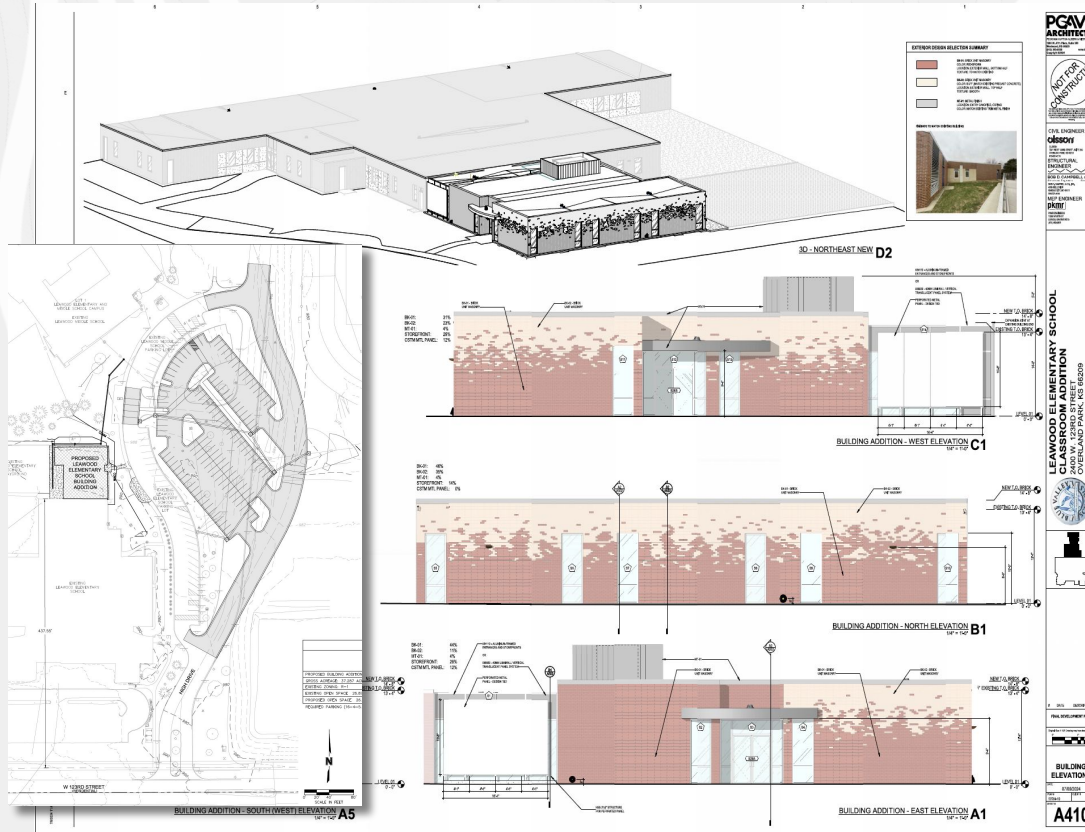

- Anticipated Start November 2024
- Anticipated Completion August 2025
- Includes removal of mobile and additional parking



Cedar Hills Elementary Classroom Addition

BOND 2023




- **Anticipated Start
November 2024**
- **Anticipated
Completion
August 2025**
- **Additions at 2
pods allows for
removal of 2
mobiles**




Blue Valley North Performing Arts Addition

BOND 2023

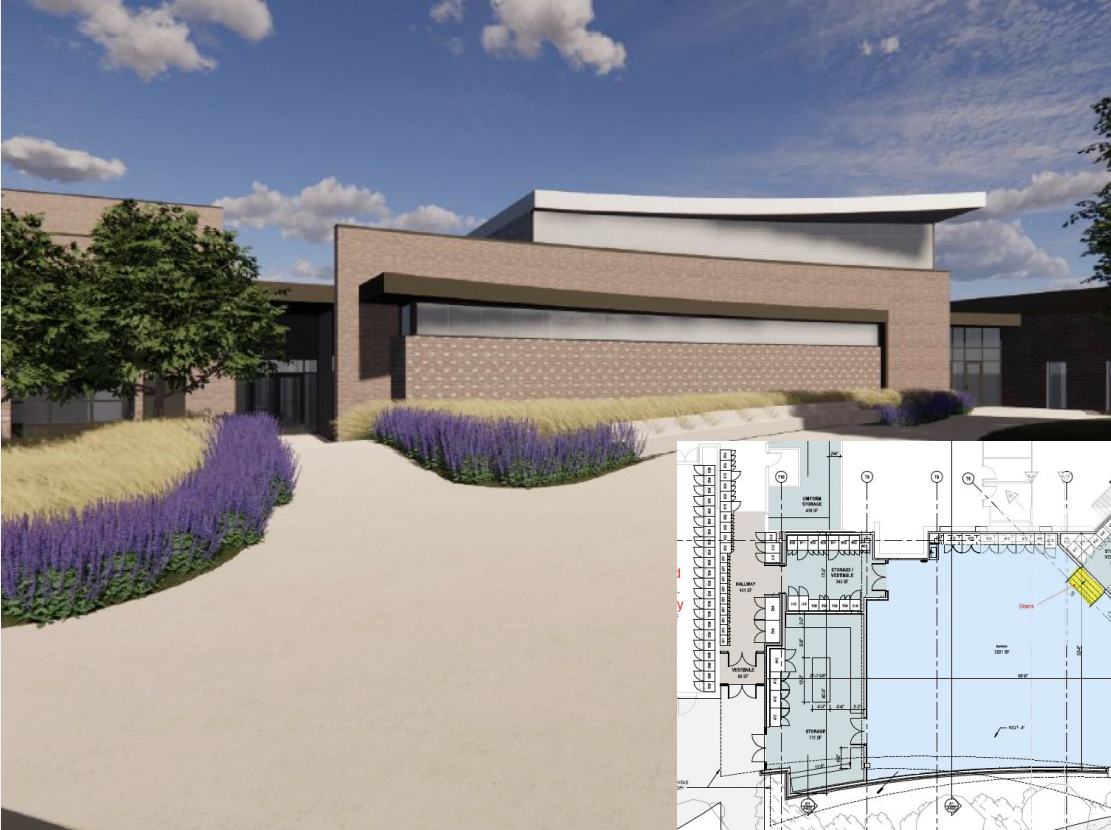

- **Anticipated Start
January 2025**
- **Anticipated
Completion
July 2025**

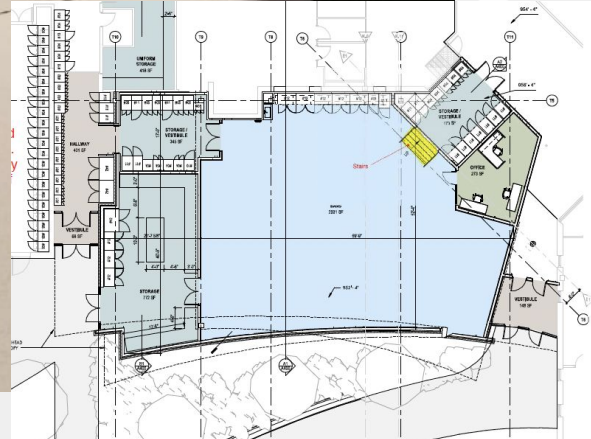

Pleasant Ridge Multipurpose Addition

BOND 2023



- **Anticipated Start
April 2025**
- **Anticipated
Completion
January 2026**



Blue Valley High Weight Room Addition

BOND 2023




- **Anticipated Start
December 2025**
- **Anticipated
Completion
August 2026**



CTE Culinary Upgrades - All High Schools

BOND 2023

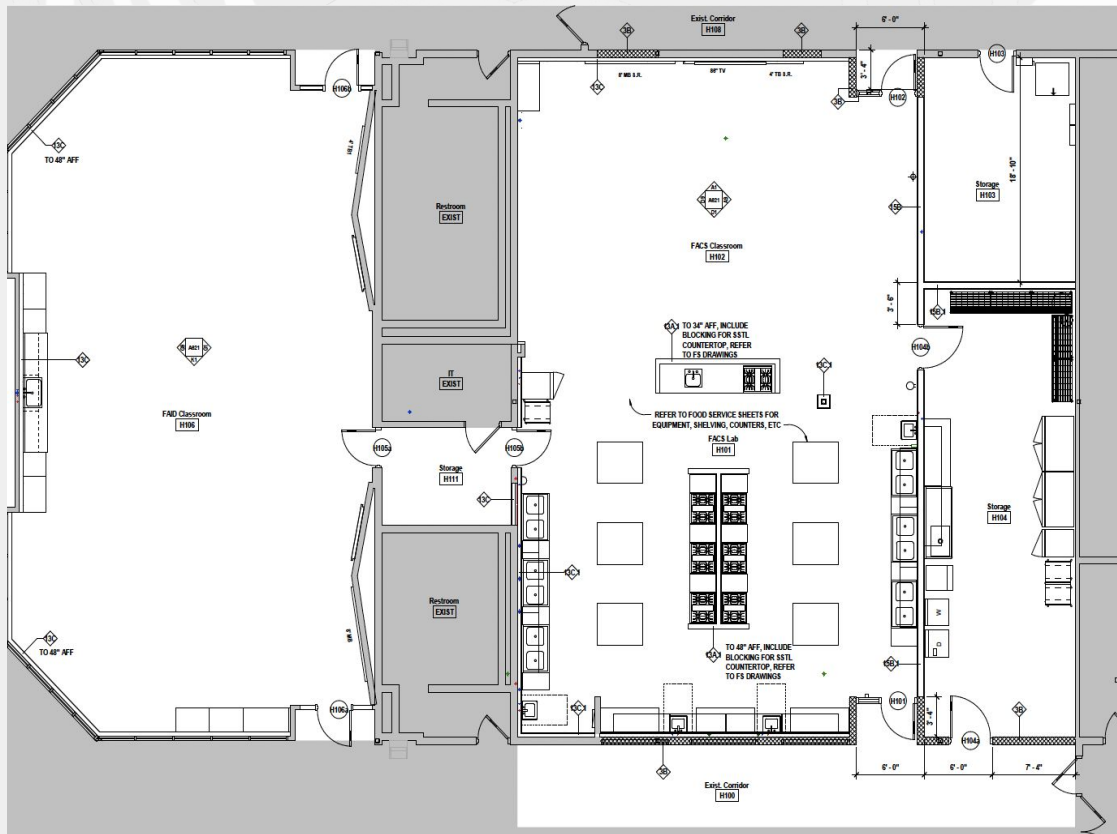

● **BVH, BVN, BVW**
Summer 2025

● **BVA, BVNW, BVSW**
Summer 2026



New Middle School

BOND 2023



STUDENTS engaged in Pre-Construction Concept Development



New Middle School

BOND 2023



- **Opens Aug. 2026**
- **Relieves Aubry Bend Middle and addresses growth in the southern part of the district**

Grant St.



175th



New Middle School

BOND 2023



Thank You.

