


# Design and Construction Update

Presentation to the  
Board of Education  
September 13, 2021



**blue** BOND  
2020 **valley**  
& Capital Outlay



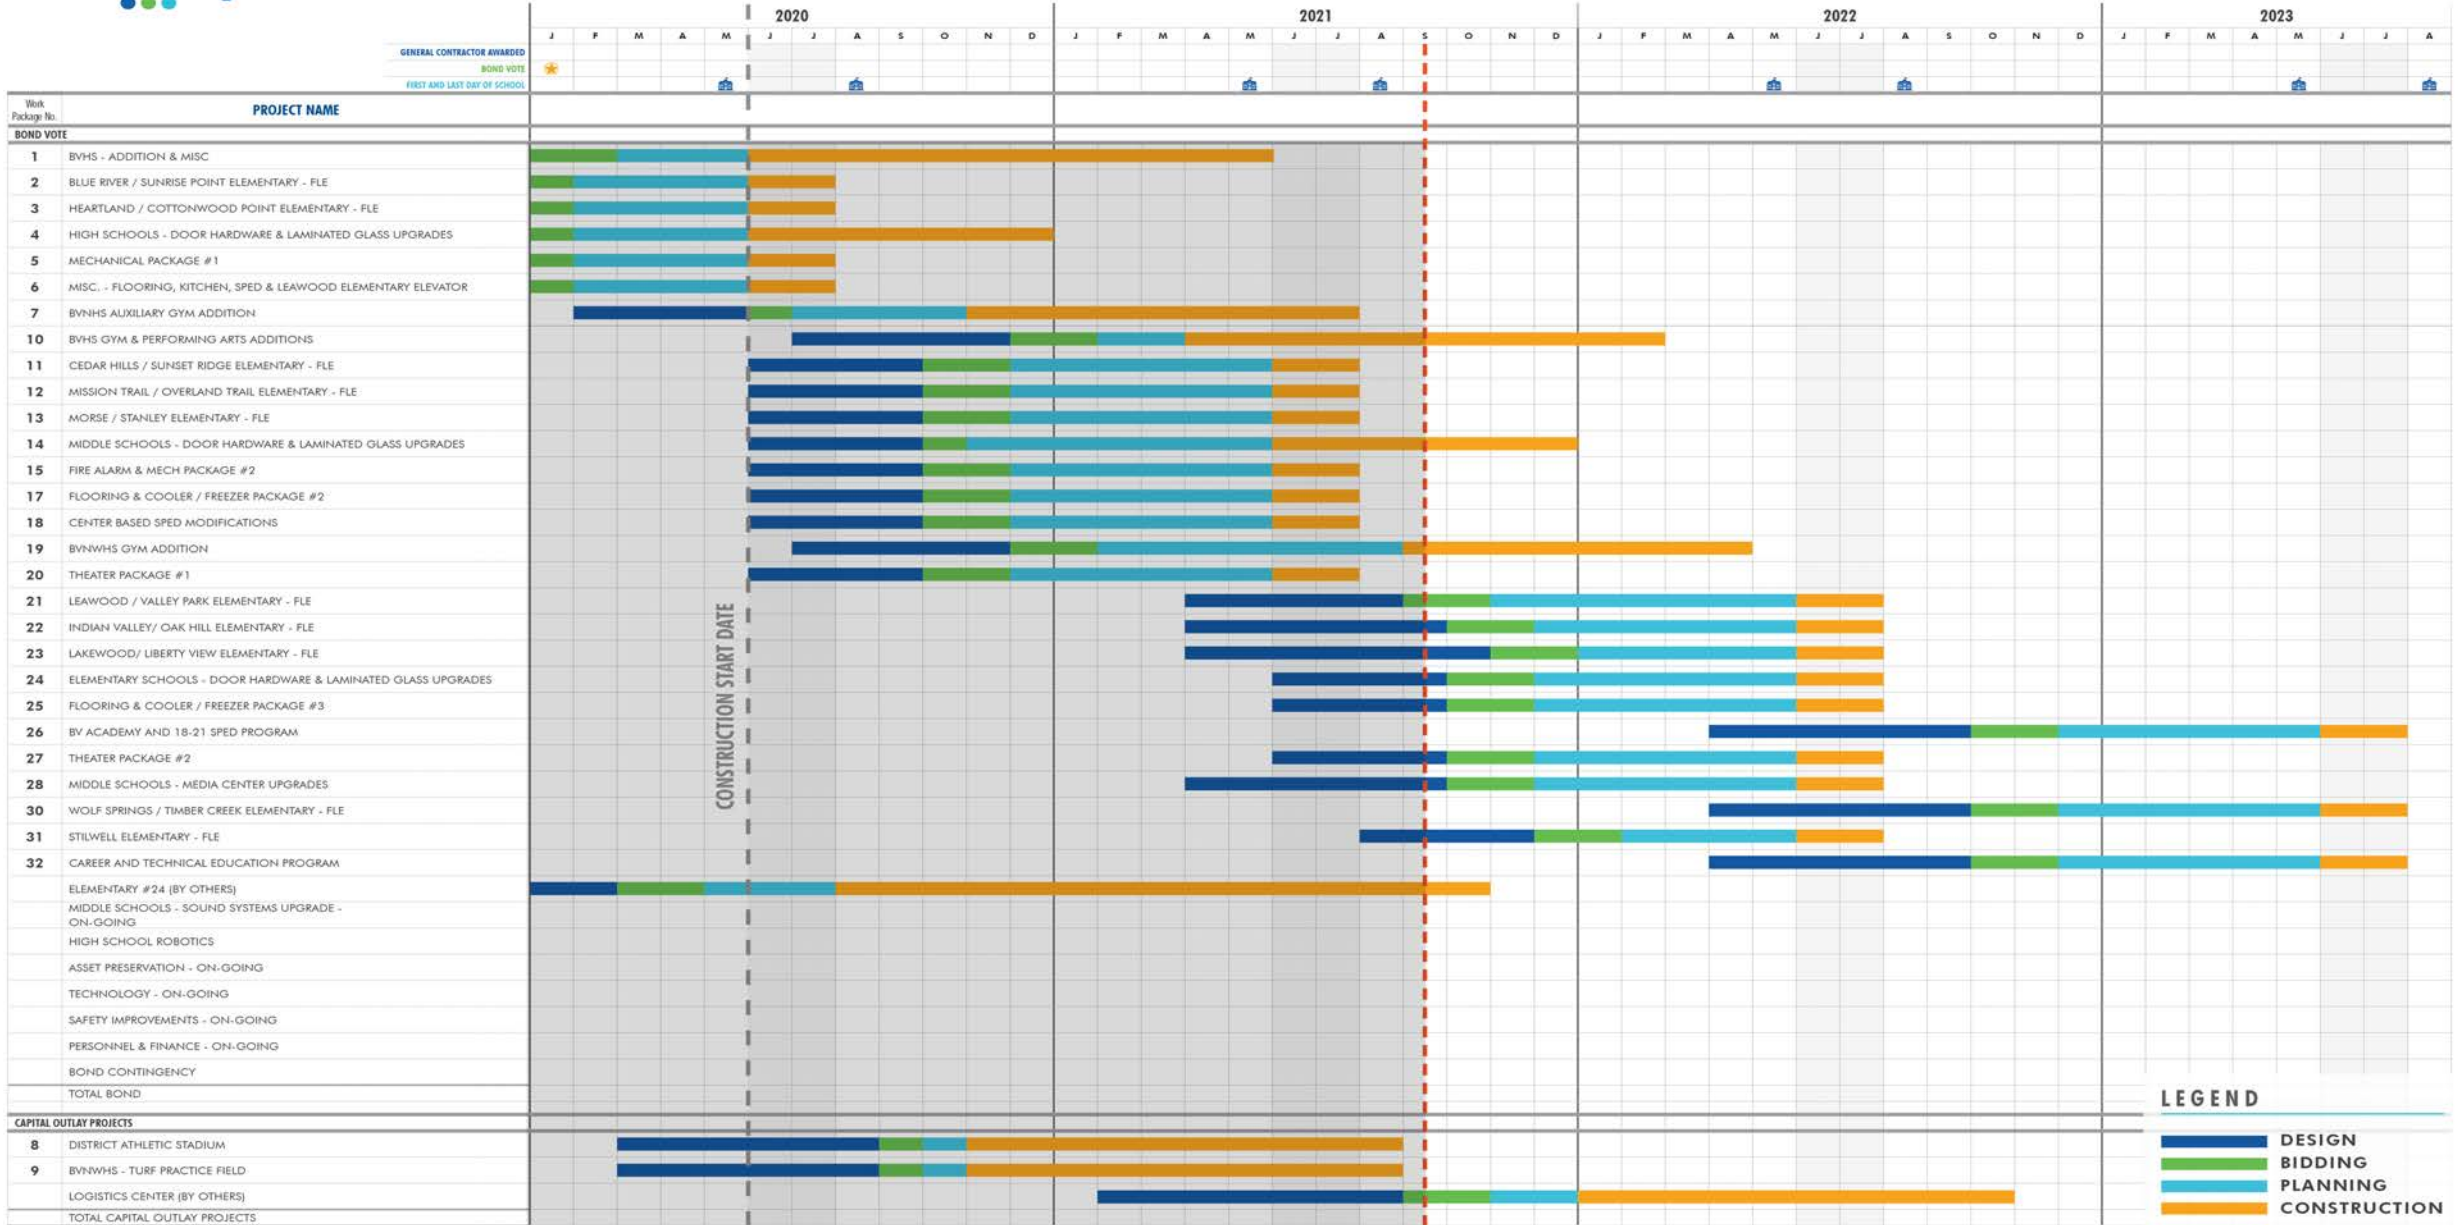

CONSTRUCTION START DATE

**LEGEND**

- DESIGN
- BIDDING
- PLANNING
- CONSTRUCTION

# WP01 - BVH Addition

Construction Schedule: Completed Spring 2021

Funding Source: 2020 Bond

Before



After




Scope: Remove 5 mobiles, build 12-classroom addition with 3 flex spaces.



# WP07 - BVN Auxiliary Gym Addition

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond

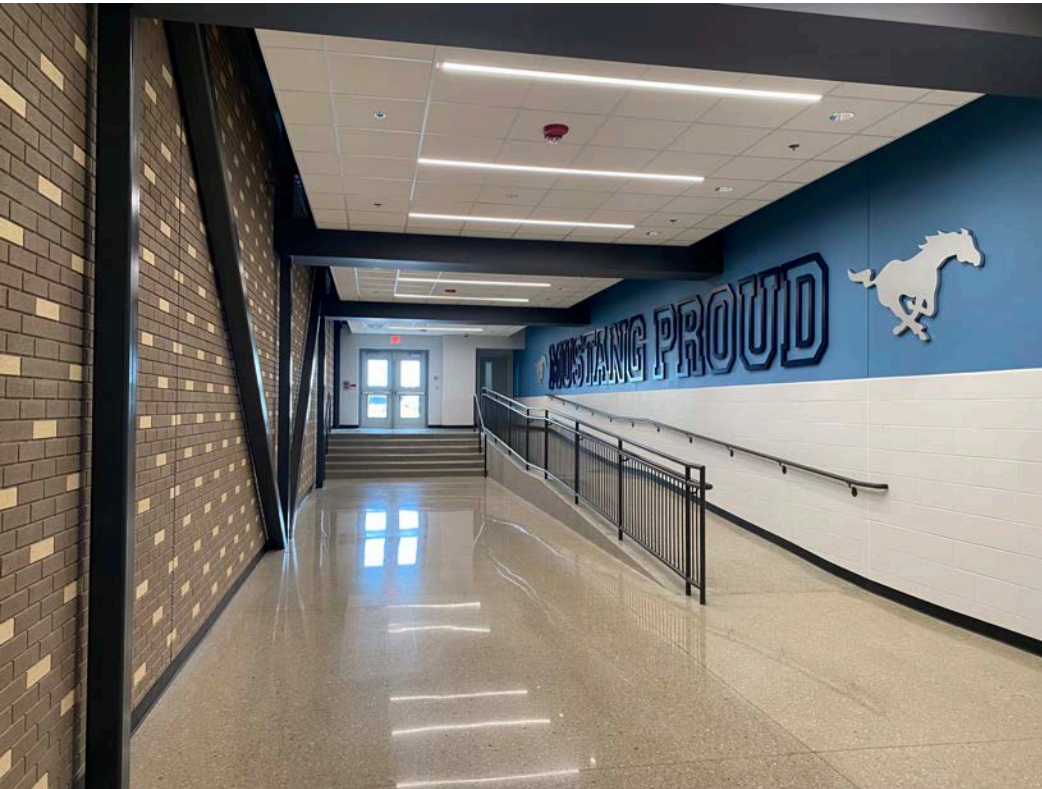

Scope: Construct new 10,000sf, 425-seat auxiliary gymnasium, ICC-500 Storm Shelter.



# WP08 - Antioch District Activities Complex

Construction Schedule: Completed Summer 2021

Funding Source: Capital Outlay



Scope: Construct new grandstand, bleachers, locker rooms, concessions, restrooms and storage and replace artificial turf field.





# WP09 - BVNW Turf Practice Field

Construction Schedule: Completed Spring 2021

Funding Source: Capital Outlay



Scope: Convert existing natural grass practice field into artificial turf field.






# WP10 - BVH Gymnasium and Performing Arts Additions

Construction Schedule: April 2021 to March 2022

Funding Source: 2020 Bond

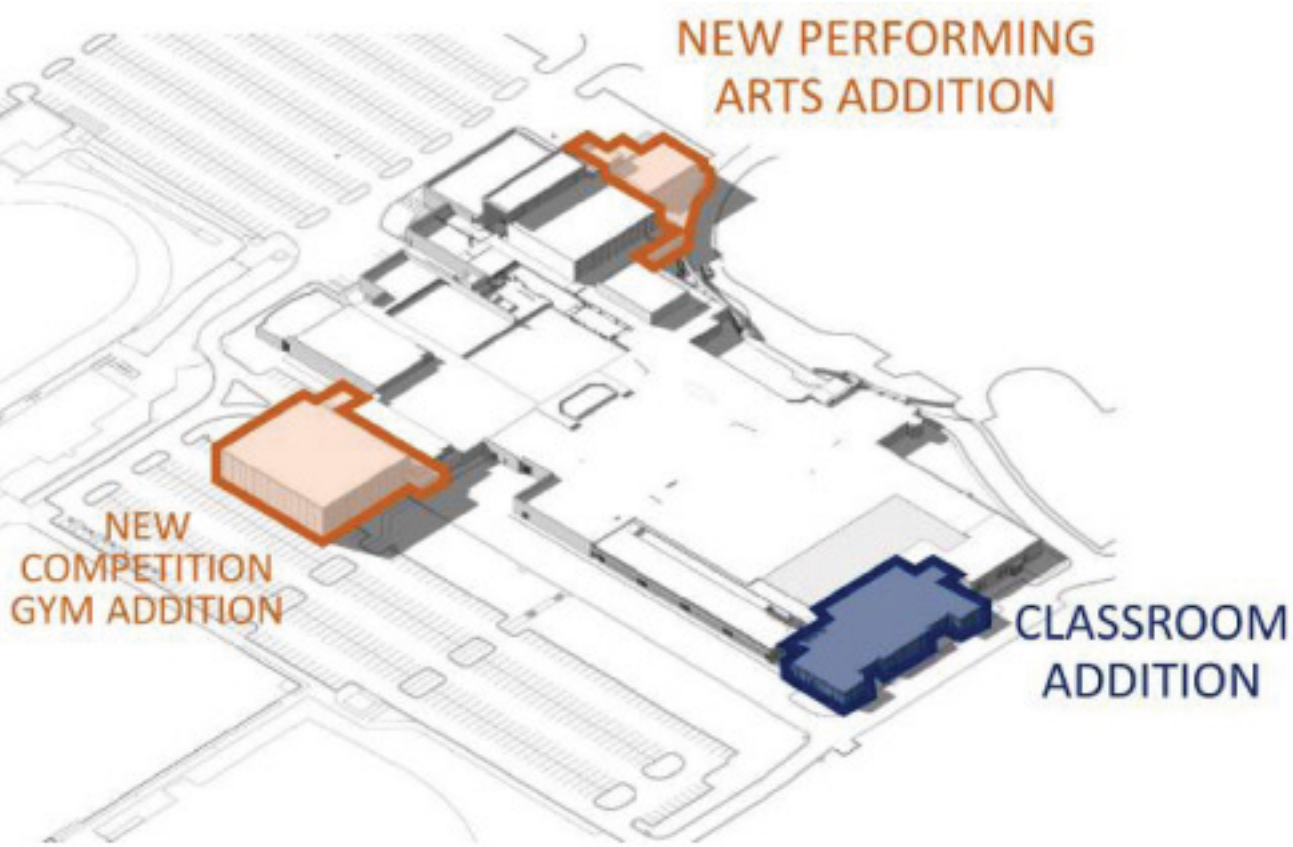

Scope: Construct new flexible theater, green room, practice rooms, storage and restrooms. Construct new 15,400sf, 2,000-seat competition gymnasium, ICC-500 Storm Shelter.



# WP11, 12, & 13- Elementary FLEs

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond



Scope: Renovate existing elementary schools (CHE, SRE, MTE, OTE, MOR, & STAN) to provide increased flexibility through operable walls.



# WP14 - MS Door Hardware and Laminated Glass

Construction Schedule: Phase 1 Completed Summer 2021, Phase 2 to be Complete Winter 2021

Funding Source: 2020 Bond



Scope: Provide thumbturn locks and impact resistant glass at classroom openings and other lockdown spaces at all Middle Schools.



# WP15 - Roofing and Major Mechanical

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond



Scope: Replaced end of life HVAC equipment and roofing at BVN, BWV, PRM, & WSC totaling 24 unit replacements. Added rooftop unit screens at BRE, BVM, HRT, IVE, and SRE.



# WP17 - Flooring, Kitchen Cooler/Freezer

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond



Scope: Polished concrete, carpet, and resinous flooring work at BRE, LKE, OTE, VPE, BVM & OTM. Kitchen cooler renovations at BVW, CHE, MTE, MOR, OMS, PRM and SRE.



# WP18 - SPED Improvements

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond




Scope: Renovated existing SPED spaces at OTM, BVM, STIL and Access House.



# WP20 - Theater Improvements

Construction Schedule: Completed Summer 2021

Funding Source: 2020 Bond

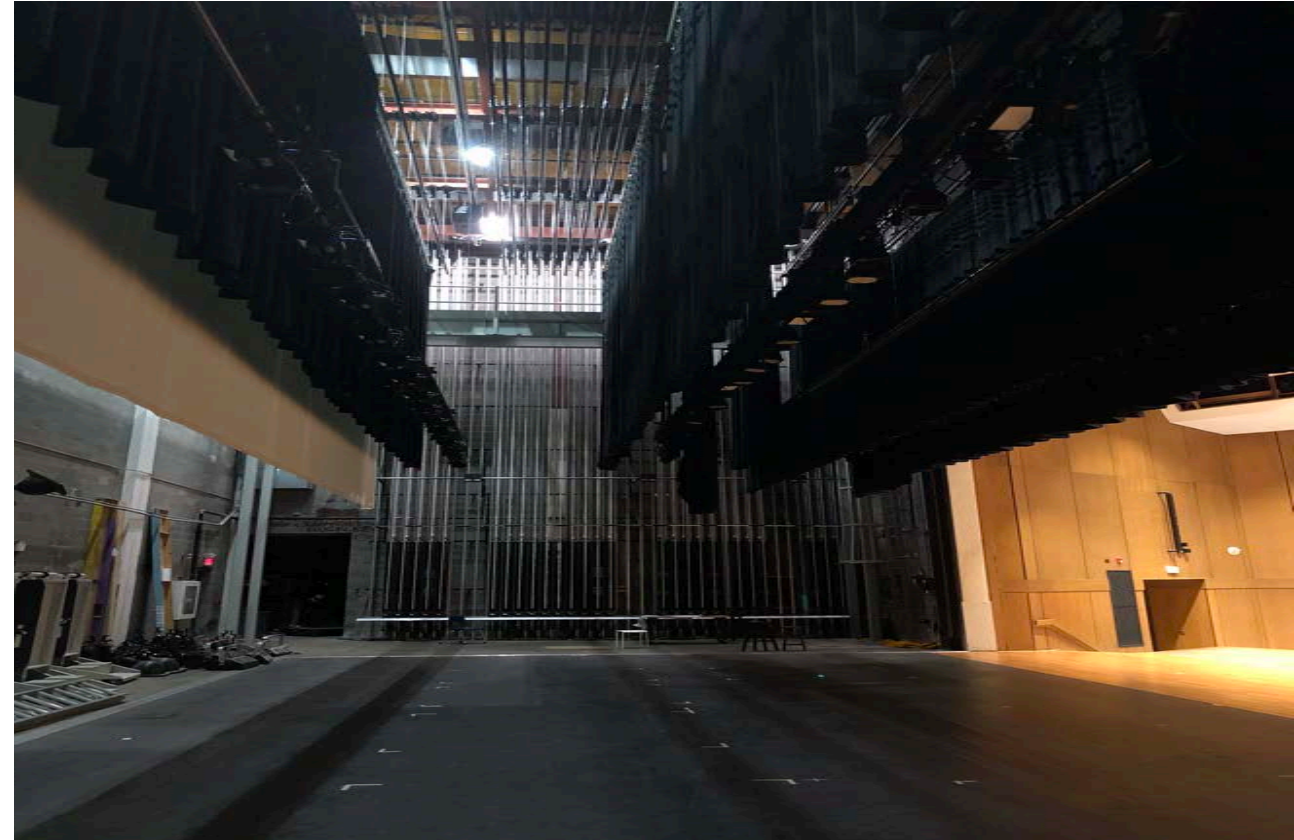

Scope: Safety and lighting improvements to theater spaces at HMS, LMS, OTM, PRM, PSM, BVN and BVW.



# Elementary #24

Funding Source: 2020 Bond



Scope: Construct new 67,000sf, 575-student elementary school with 24 classrooms, 3 dedicated SPED rooms, and flexible spaces throughout.



# Upcoming Projects

## Bond 2020

BVNW High School Gymnasium Addition  
FLE Renovations: LES, VPE, IVE, OHE, LKE, and LVE  
Elementary School Security Door & Hardware Upgrades  
Flooring and Kitchen Upgrades  
Theater Safety Improvements  
Media Center Improvements: OMS and PRM  
Fire Alarm Upgrades  
Roofing and Mechanical Upgrades

## Capital Outlay

Blue Valley Logistics Center



**Thank You.**
